

Clay County District Schools

Middleburg Elementary School

Renovation/Remodel Building 7



HARVARD - JOLLY


ARCHITECTURE

DESIGNING POSSIBILITIES SINCE 1938

Project Site




Project Site

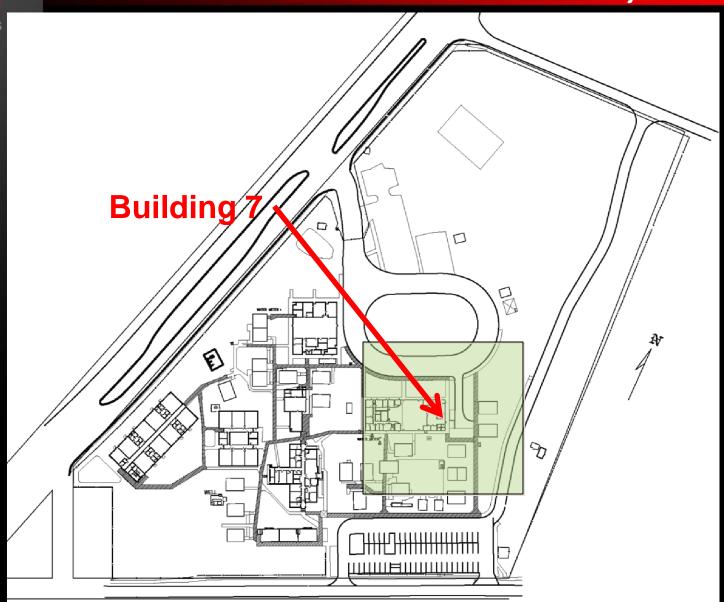





Selected Option



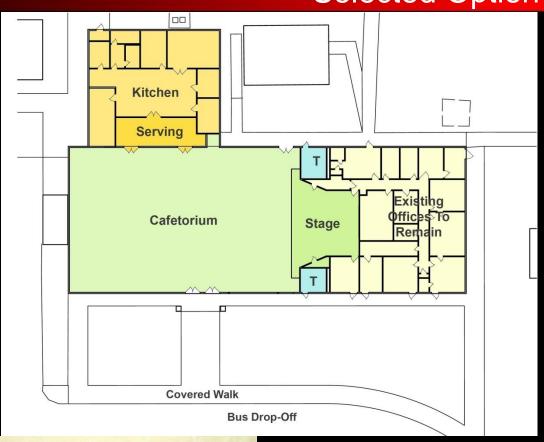





Site Plan

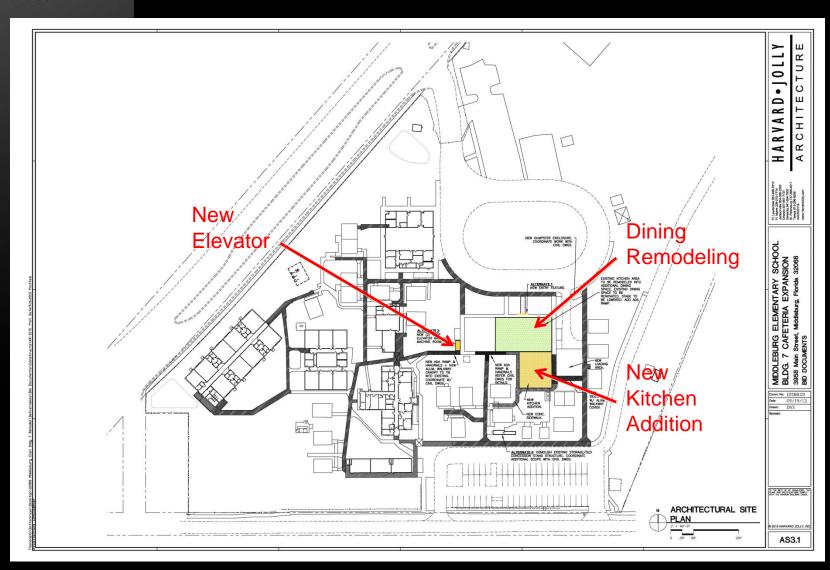

Floor Plan

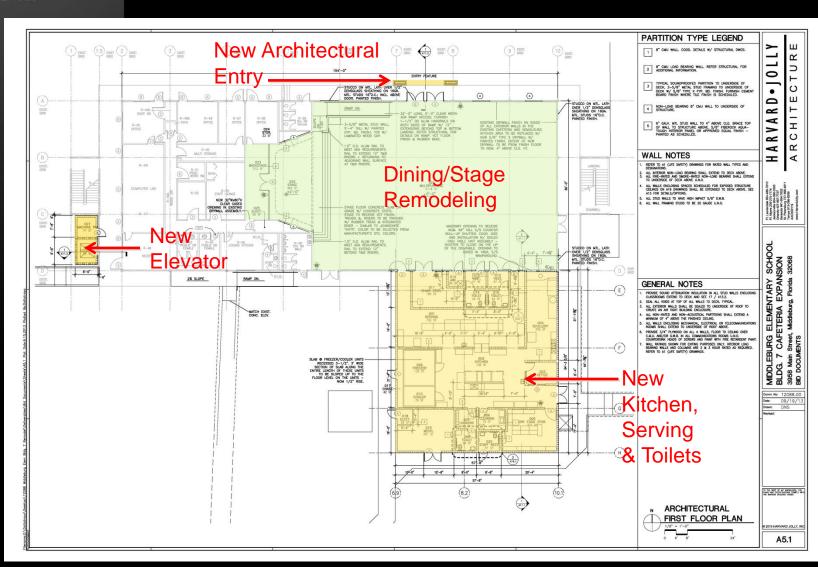

Elevations

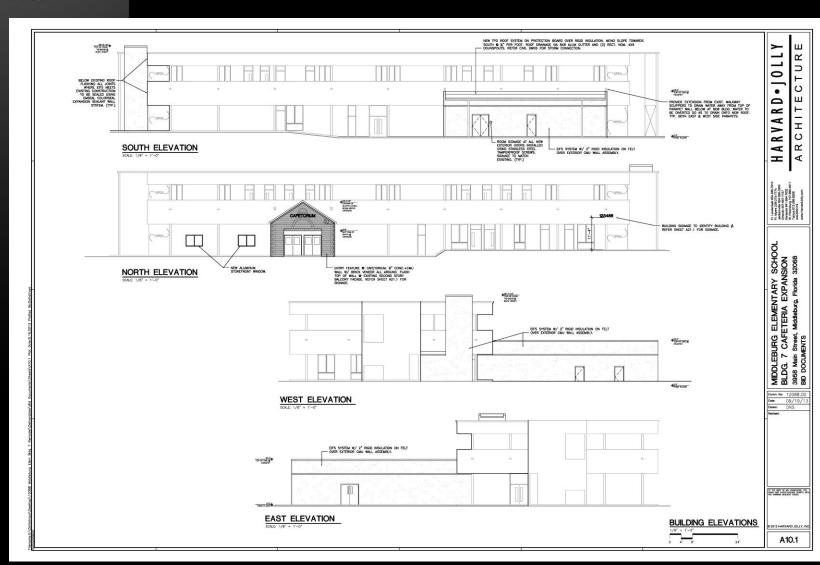

HARVARD - JOLLY

Project Schedule

DESIGNING POSSIBILITIES SINCE 1938

Middleburg Elementary School Building 7 Cafeteria Expansion

Sept 19, 2013

Activity	Duration	Activity Begin Date	Activity End Date	2013 Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	2014 Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
Notice To Proceed for Design	1	8 Jan' 2013	8 Jan' 2013																					
Schematic Design	30	8 Jan' 2013	6 Feb' 2013												Ì									
CCDS Review		7 Feb' 2013	1 Mar 13																					
Preliminary Design	60	2 Mar 13	30 Apr 13																					
CCDS Review	30	1 May 13	31 May 13																					
100% Construction Documents	65	1 Jun 13	5 Aug 13																					
CCDS Relocate Portables	53	10 Jun 13	2 Aug 13																					
CCDS Review	26	6 Aug 13	30 Aug 13																					
Bldg Permit Review	26	6 Aug 13	30 Aug 13												1									
AE Final Bid Documents	10	31 Aug 13	9 Sep 13																					
CCDS Board Backup Due	1	11 Sep 13	11 Sep 13																					
CCDS Board Approval of Final Plans	1	19 Sep 13	19 Sep 13																					
Advertisement for Bids (3, 10, 17 Oct)	35	3 Oct 13	6 Nov 13																					
Mandatory Pre-Bid Meeting	1	22 Oct 13	22 Oct 13																					
Bid Opening	1	6 Nov 13	6 Nov 13																					
CCDS Board Backup Due	1	13 Nov 13	13 Nov 13																					
CCDS Board Contract Award	1	21 Nov 13	21 Nov 13												7						į.			
Notice To Proceed for Construction	1	23 Nov 13	23 Nov 13																					
Contractor Secure Construction Area	10	23 Nov 13	1 Dec 13																		Į.			
Construct Kitchen Addition	250	23 Nov 13	30 Jul 14																					
Relocate Kitchen Equipment	7	1 Jun 14	7 Jun 14																					
Remodel Kitchen to Dining	56	5 Jun 14	30 Jul 14																					
Renovate Dining & Stage	56	5 Jun 14	30 Jul 14																					
Substantial Completion	1	30 Jul 14	30 Jul 14																					
Final Completion	30	31 Jul 14	29 Aug 14																					

Last Day for Teachers

Teachers Back to School Students Back to School

Thanksgiving Break Monday Nov 25 - Friday Nov 29, 20

Last Day for Students
Teachers Back to School
Students Back to School

Tuesday August 6, 2013 Tuesday August 13, 2013 Monday Nov 25 - Friday Nov 29, 2013

Wednesday June 4, 2014
Wednesday August 5, 2014
Tuesday August 12, 2014

Thursday June 6, 2013

HARVARD-JOLLY

HARVARD • JOLLY

DESIGNING POSSIBILITIES **SINCE 1938**

Statement of Probable Cost

Middleburg Elementary School Building 7 Cafeteria Expansion

Statement of Probable Cost

<u>Construction Cost Projection – Phase III Final Documents</u> September 12, 2013

Cafeteria Expansion

New Kitchen, Serving, Toilets and Chair Storage,

Fire Protection System – Entire First Floor,

	ADA Access	to First Floor.	Associated Sitework
--	------------	-----------------	---------------------

ADA Access to First Floor, Associated Sitework					
Total Projected Base Bid	\$1,316,500				
By School Board of Clay County					
New Walk in Refrigerator/Freezer	\$ 47,000				
New Kitchen Hood	\$ 30,000				
Total Projected Base Bid + SBCC Costs	\$1,393,500				
Additive Alternates					
#1 Architectural Entry Feature	\$ 45,000				
#2 Elevator	\$ 100,000				
#3 Tie HVAC Controls into BAS	\$ 30,000				
#4 Demo Existing Storage Shed	\$ 2,500				
Total Projected Construction Cost	\$1,571,000				

Notes

Existing Relocatables relocated by District.

Food Service Equipment to be relocated from Existing. Other Kitchen Equipment by District.

Existing Student Toilets adjacent Dining Room to remain as is.



Clay County District Schools

Middleburg Elementary School

Renovation/Remodel Building 7

